


## UCPORI – muutostyöt 2026



### VK 23


- 126 tilan tukikehikon ja lattian purku suoritettu → The support structure and floor demolition works in Room 126 have been completed.
- 126 tilan ja 100 aulan välisen seinän aukotustyöt käynnissä → Wall opening works between Room 126 and the 100 lobby area are in progress.
- Lohko 2 töiden valmistelut valmistuneet → Preparatory works for Block 2 have been completed.
- Lohko 2, 129/130 wc tilojen vesikalusteiden irtikytkentä → Disconnection of plumbing fixtures in the WC facilities 129/130 in Block 2.

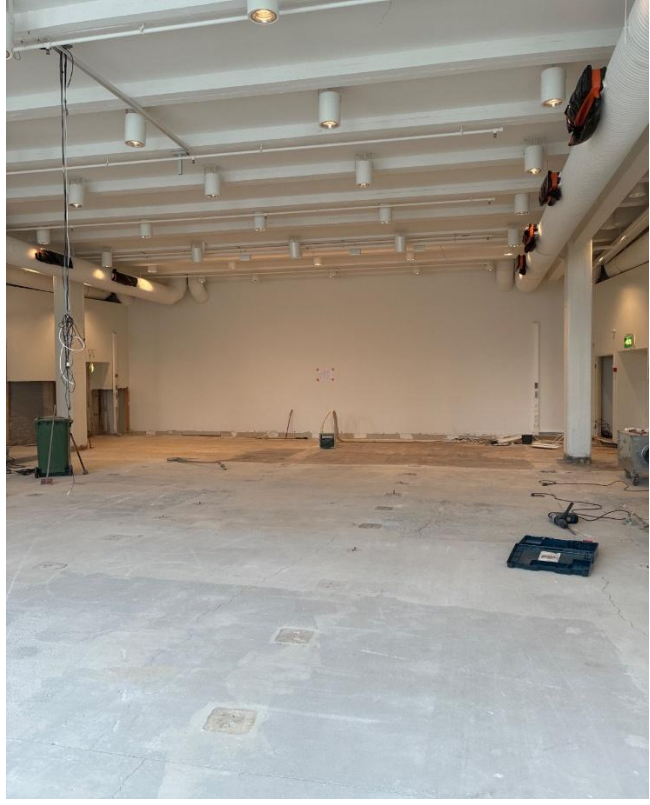

126 tilan kehikon purku työ suoritettu, yleinen siisteys tilassa hyvä. → The demolition of the support framework in Room 126 has been completed, and site cleanliness is at a good level.



126- ja 100 aulan välisen seinän suojaus- ja aukotustyö tehty → Protection and wall opening works between Room 126 and the 100 lobby area have been completed.

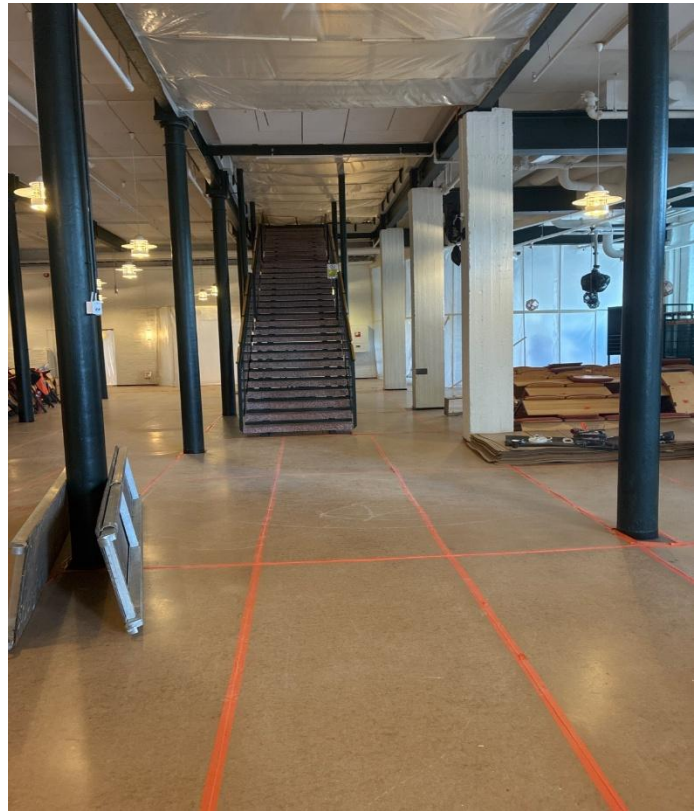

Työmaan yleinen siisteys hyvällä tasolla → The overall condition and cleanliness of the site are good.

## VK 24 Tavoitteet – Objective

- 125 auditorion penkkien purku → 125 auditorium seating demolition works
- 126 tilan lattian valutöiden valmistelu, aloitus 8.6 → Preparatory works for the floor concrete casting in Room 126, starting on 8 June.
- Lohko 2 purkutöiden aloitus → Commencement of demolition works in Block 2.
